



AGNESS ROAD RECONSTRUCTION PHASE 2


Past Week:

Laskey-Clifton completed construction of the Geogrid patch at STA 32+800 and paved over the top of it. Chip Seal operations began in the beginning of the week at the end of the project making about 14 miles of progress (both lanes) towards the beginning of the project. Sweeping operations began to clean up the loose rock on the surface of the road. Laskey-Clifton completed shoulder work at STA 21+300, completing correction work due to winter storm damage.

This Week:

Laskey-Clifton will complete the Surface Treatment, Chip Seal around the middle of the week and continue sweeping the excess aggregate material. Laskey Clifton may be looking to begin the fog seal operations around the end of the week depending on how fast the Chip Seal and sweeping finish, or else the fog seal will begin during the early part of next week.

Below: Chip Seal application

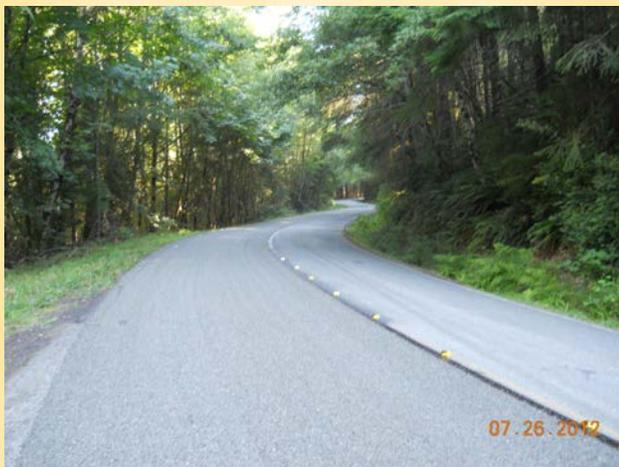

Below: Chip Seal application



Project Engineer CO-WFLHD: Glenn T. Kutzera

Construction Inspectors: Nathan Jones

Clyde Taylor

Number: (406) 471-8762

Contractor: Laskey-Clifton Corp.

75355 HW 101, P.O. Box 50

Reedsport OR, 97467

Office Number: 541-271- 2213
