

Western Federal Lands Highway Division – Federal Highway Administration



Ken Oltmann, CMPM
Ken.Oltmann@q.com
PO Box 1403
Bandon, OR 97411
(541) 329-0394
Fax (541) 329-0395



August 4th, 2011

Progress Report

The main activity for the week of August 1st was, the contractor trenched in 772 ft of 5 inch conduit and set 2 vaults this week. The contractor finished removing material from the surcharge areas and continued building fills from station 35+00 to 64+00. The contractor started removing the material from the approach road to the USFWS Head Quarters office this week. The surveyors were on project this week setting grade stakes from station 35+00 to 64+00 contractor plans to construct this area to grade this week. They are getting the shoulders of the road ready to start building the small fills from station 70+00 to 120+00 this will be on going for the next two weeks. Expect some delays and watch for equipment on the road the project is under pilot car use the operation is spread out along the full length of the project. This report will be updated as more activities begin.

Project Photo's



Construction activities for the North Bank Lane portion of the project began 2010 and the road construction activities will be completed in the fall of 2011. Once construction begins, weekly newsletters will be posted below providing road closure, delays, and other pertinent information regarding the project.

Go online for more information and to read old newsletters at <http://www.wfl.fhwa.dot.gov/projects/>




Contractor's Work Schedule

Monday – Thursday: Hours: 7am – 5pm
Survey Crews maybe working Monday-Fridays:

Traffic Delay Information

There will not be any construction activity on North Bank Lane until the contractor returns to the project. We will have surveyors on the project.



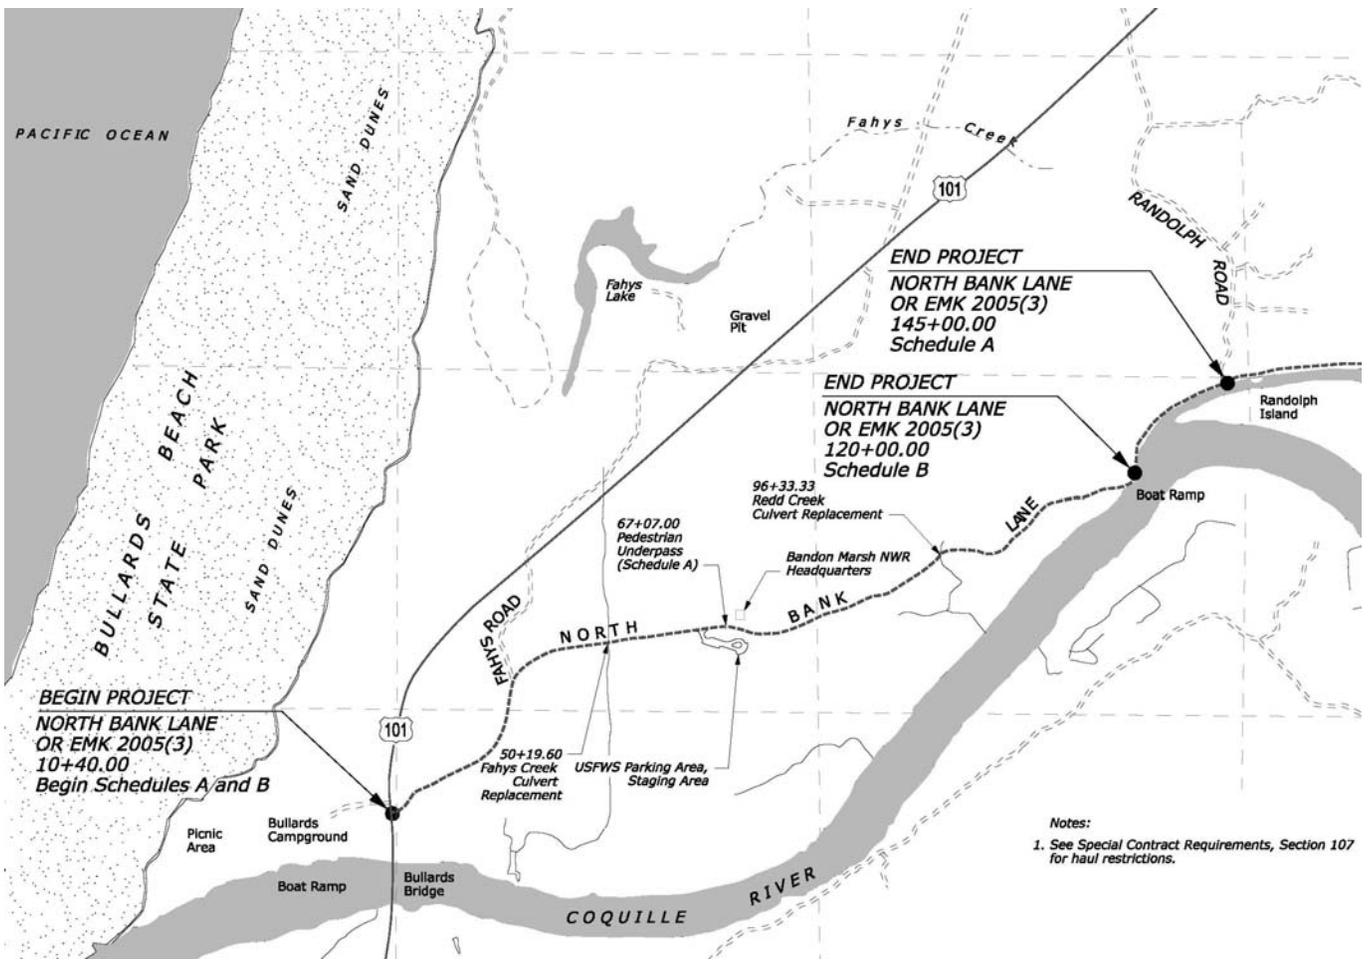

Notes:
 1. See Special Contract Requirements, Section 107 for haul restrictions.
