



Ken Oltmann, CPM  
Ken.Oltmann@q.com  
PO Box 1403  
Bandon, OR 97411  
(541) 329-0394  
Fax (541) 329-0395



August 26th, 2011

### Progress Report

The main activity for the week of August 22nd was, the contractor finished all of the trenching except two areas that need spliced one at Redd's Creek and one at Fahys creek. The contractor installed culverts this week at two locations. The contractor finished removing material from the new approach road to the USFWS Head Quarters office this week. PPL was on the project on Monday removing the old poles in the area listed above all the poles are removed now and the wires are moved to the new poles. The contractor began work on the pedestrian culvert stairway by clearing and excavating around both the inlet and the outlet of the culvert and he completed the excavation for the stairs. Both areas were over excavated to allow room for the contractor to build his forms for the walls. The contractor is build fills and finishing grade from station 35+00 to 65+00. The contractor plans to construct the de-cell lane at HWY 101 next week. Expect some delays and watch for equipment on the road the project is under pilot car use the operation is spread out along the full length of the project. This report will be updated as more activities begin.

### Project Photo's



Construction activities for the North Bank Lane portion of the project began 2010 and the road construction activities will be completed in the fall of 2011. Once construction begins, weekly newsletters will be posted below providing road closure, delays, and other pertinent information regarding the project.

Go online for more information and to read old newsletters at <http://www.wfl.fhwa.dot.gov/projects/>




#### **Contractor's Work Schedule**

Monday – Thursday: Hours: 7am – 5pm  
Survey Crews maybe working Monday-Fridays:

#### **Traffic Delay Information**

There will not be any construction activity on North Bank Lane until the contractor returns to the project. We will have surveyors on the project.



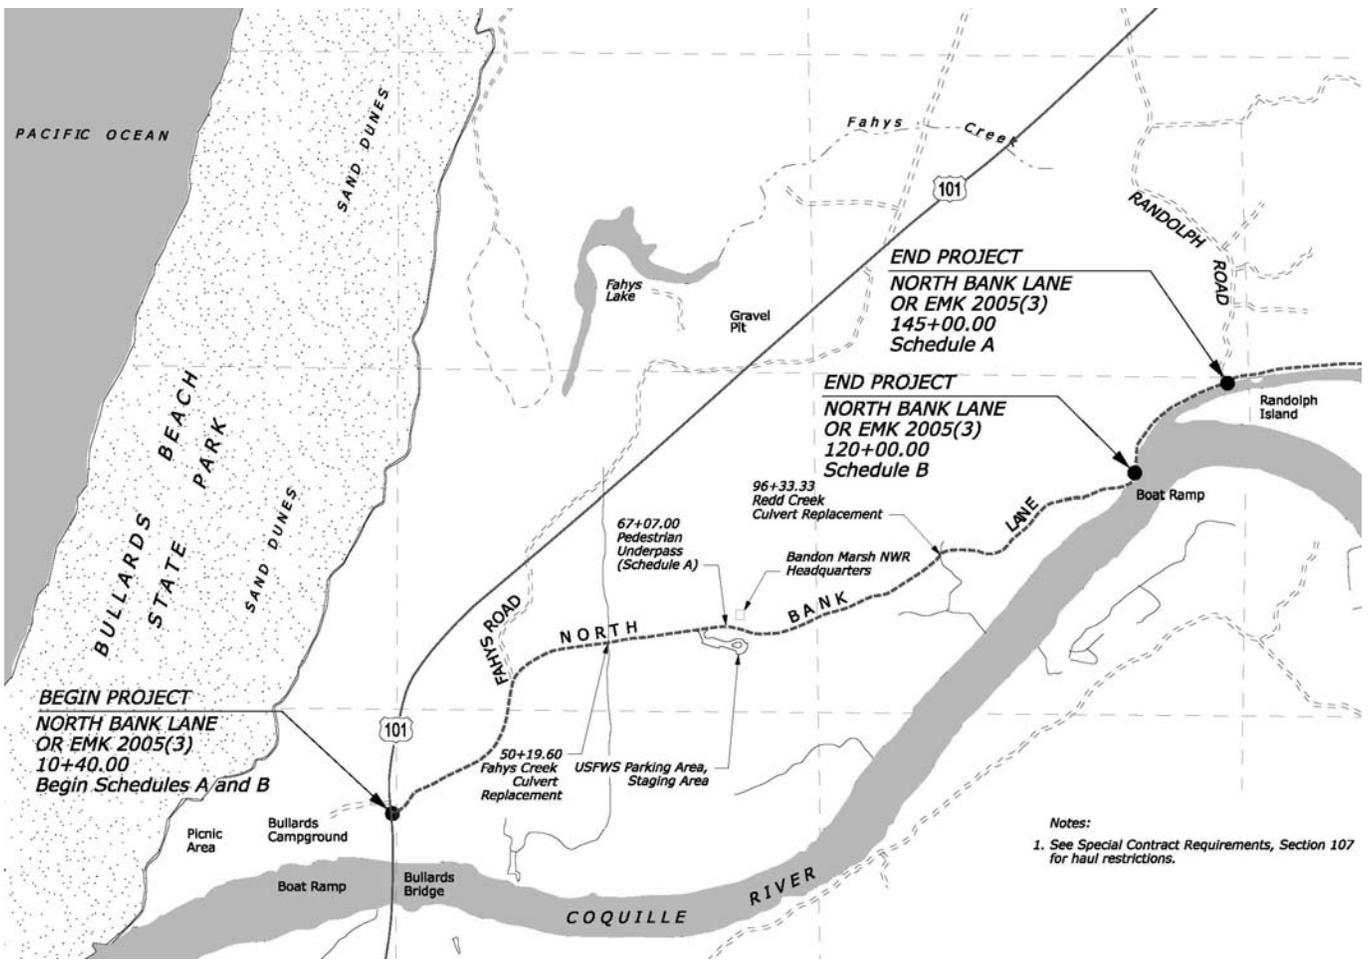

Notes:  
 1. See Special Contract Requirements, Section 107 for haul restrictions.
